




ECP



# NATURAL GAS POWER PLANT PROGRESSES REPORT 2025



December 3, 2025

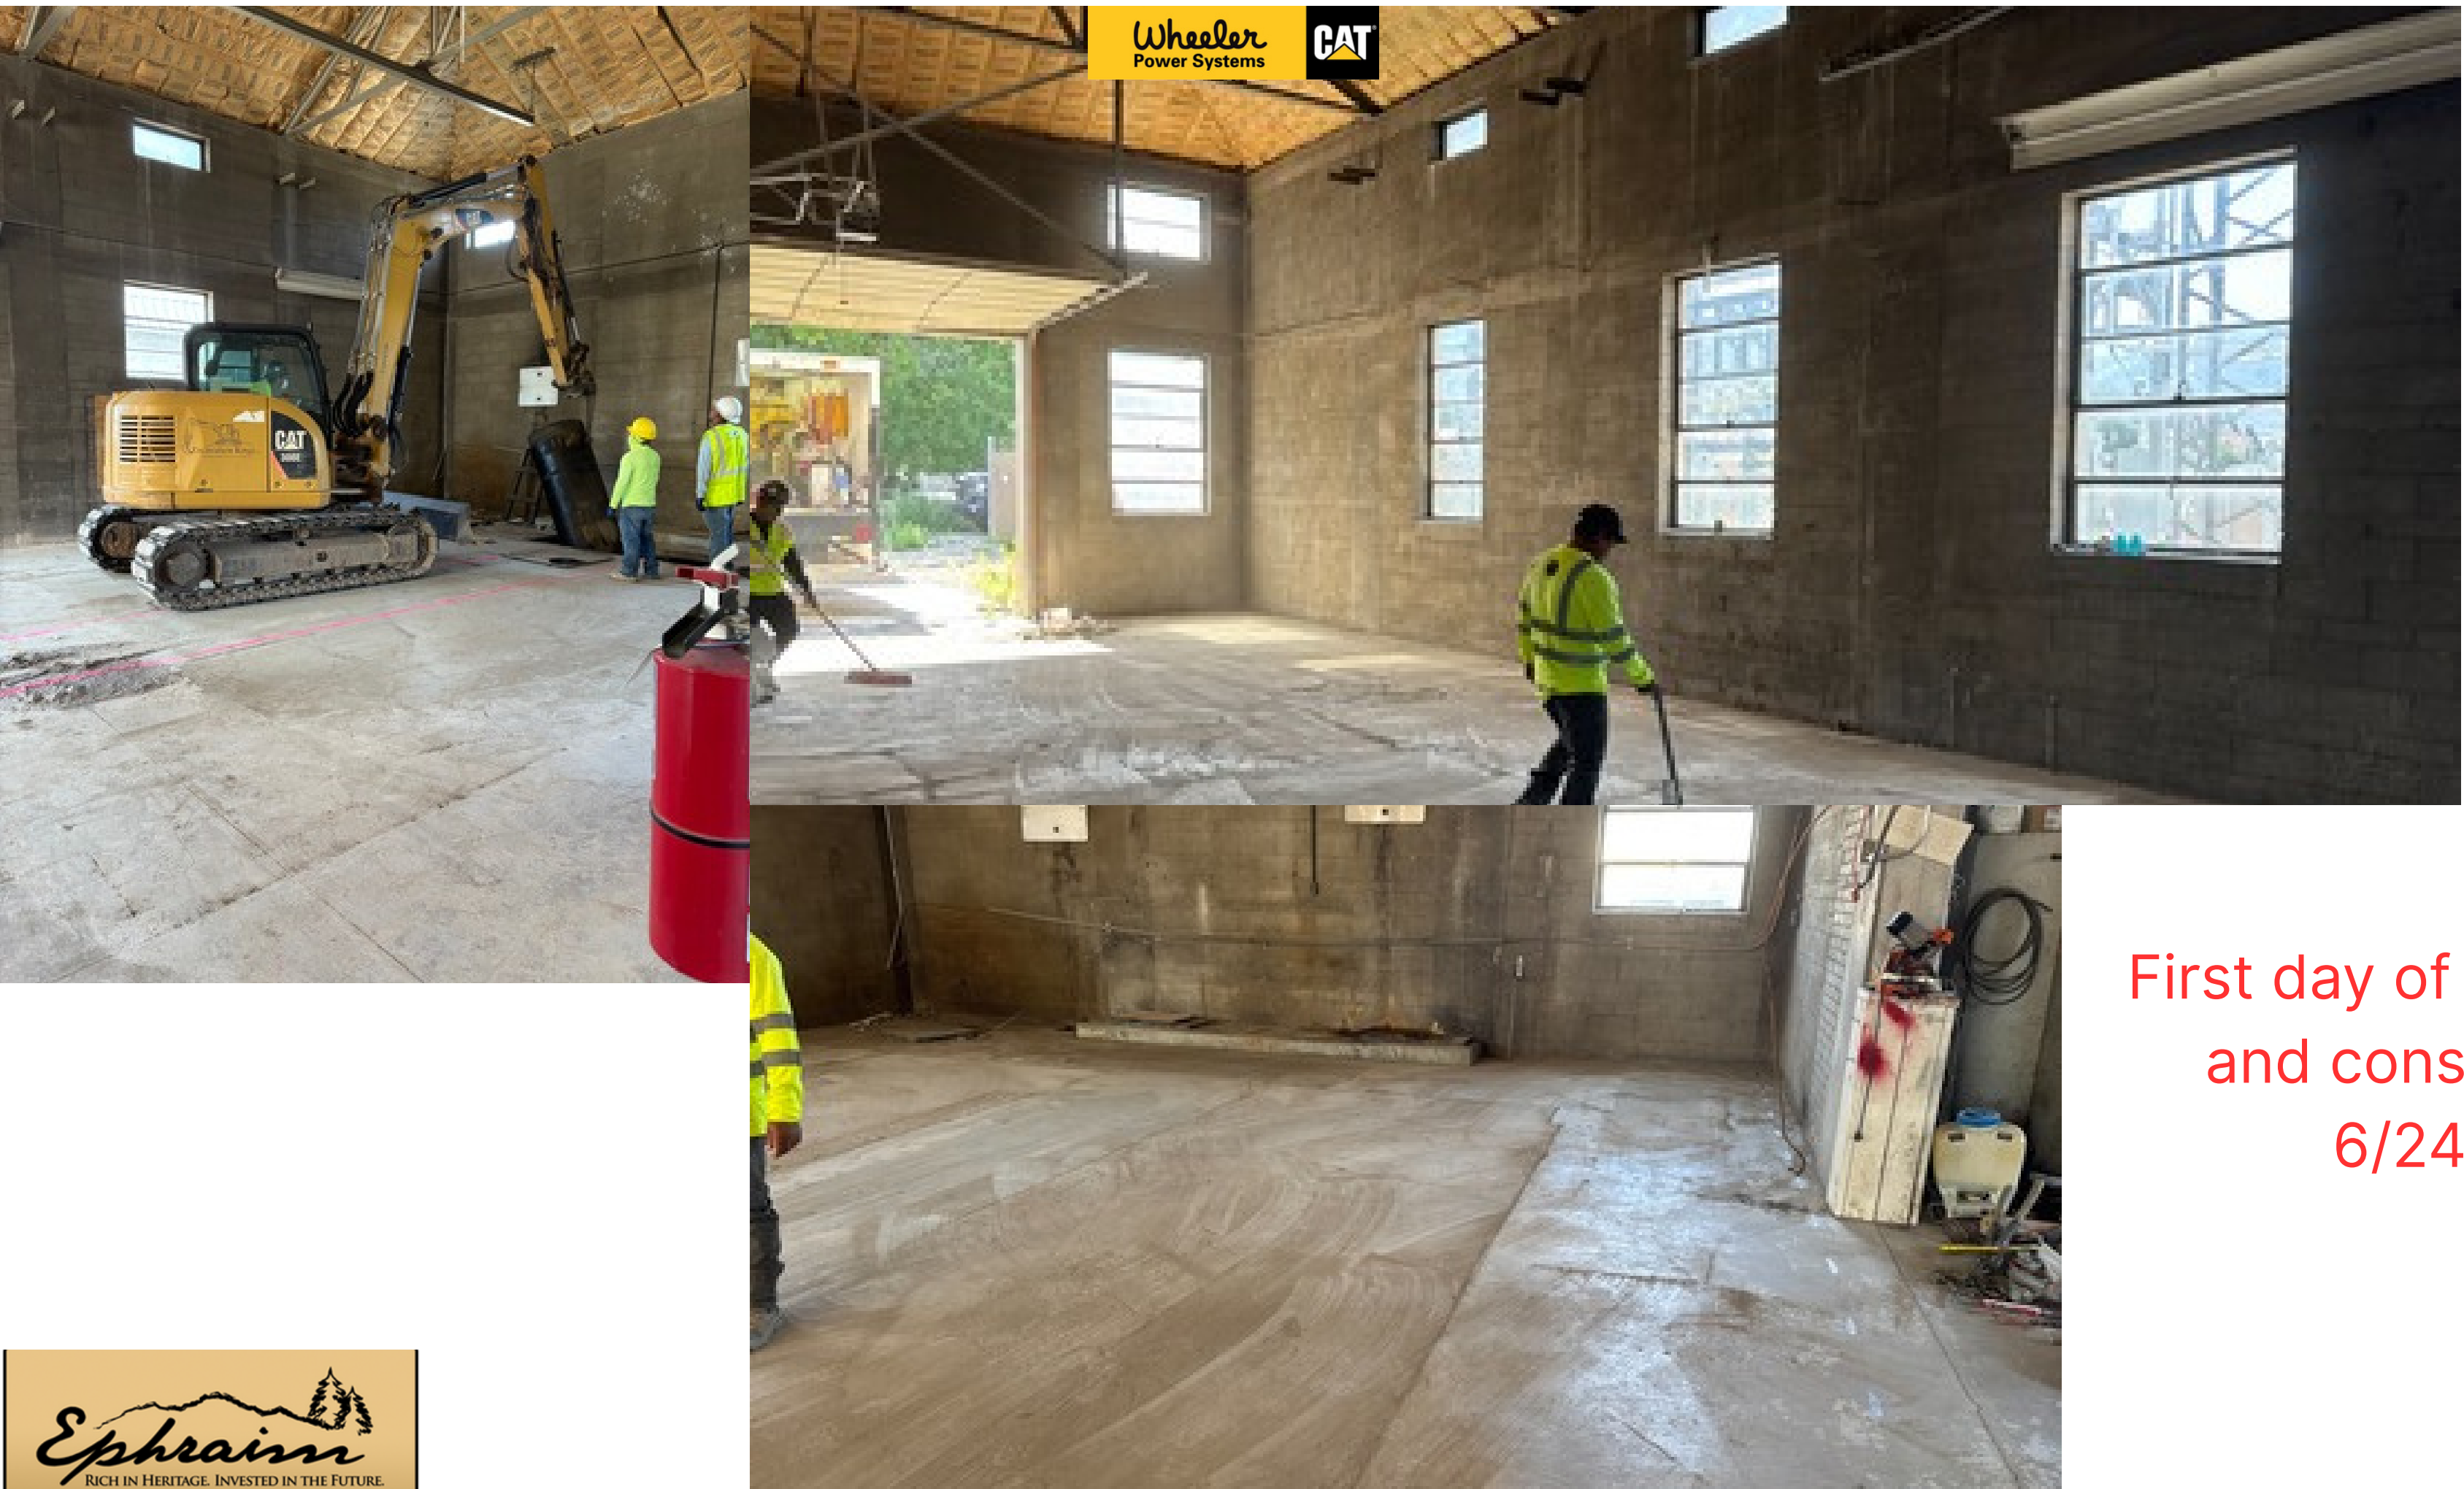

First day of demolition  
and construction  
6/24/25



## Concrete demolition inside building




## A few surprises along the way



Old oil tanks





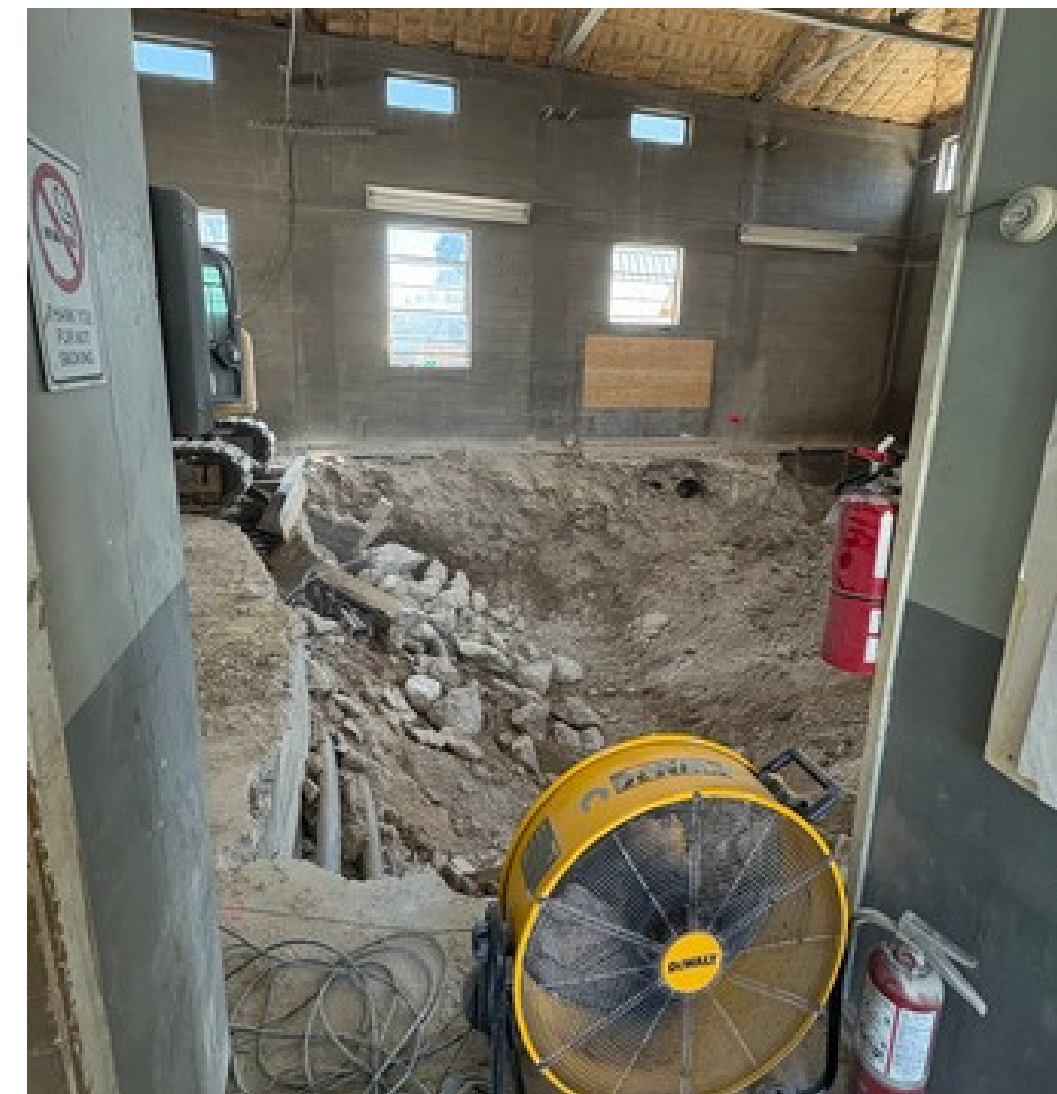

July 7<sup>th</sup> through the 11th







Concrete all removed  
from building



Ready for radiator pad



Middle July



Last of giant concrete pile





Ground grid installed



Pad ready for road base west of building

Mid  
July



New fill-ready for conduits



Old septic tank removed

# Late July



First of many Conduits



Bathroom remodel



Radiator and swamp cooler pad



Stands being built for conduits





Start of first generator pad

# August



Bathroom being  
replumbed





# Late August early September



Conduits for main power to  
the building



Trenching for main power to building done by  
Ephraim power




Finally received some rain

Early September



First generator pad ready for concrete

Core holes for conduit

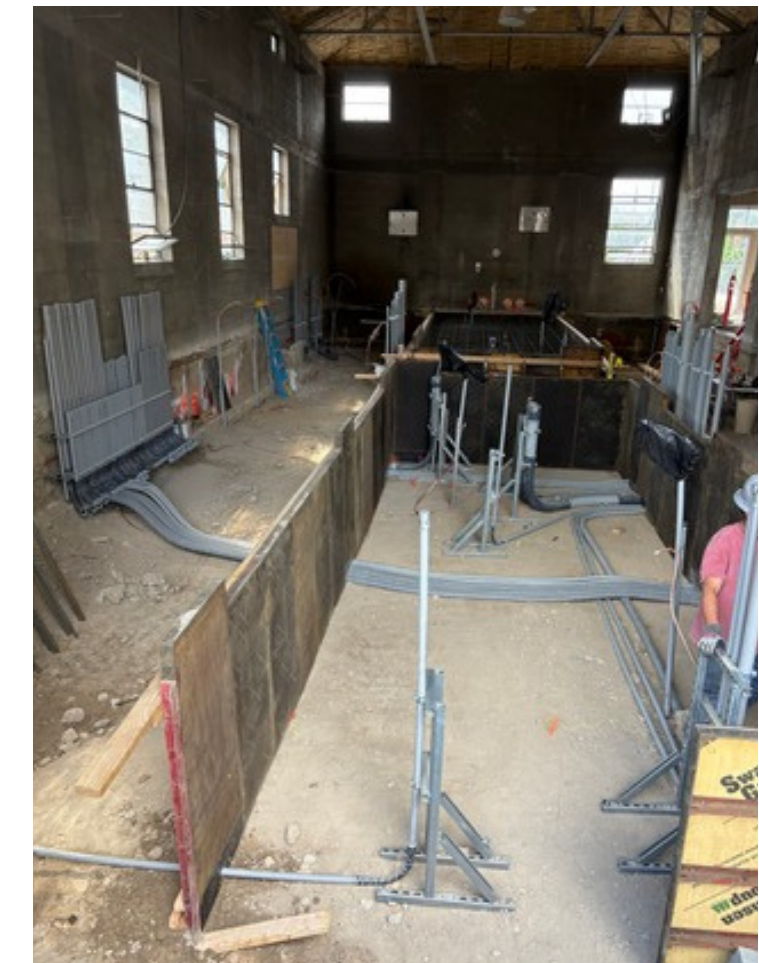

Second gen pad being built







Generator pads all poured and concrete finished  
40 yards in each pad. 9/15/25





Start of main conduit install  
9/29/25



4" Gas stub installed 9/17/25



Radiator,Oxy catalyst pad being poured  
10/6/25






Conduits being heated to be bent for  
placement 9/29/25




10/16/25



Amazing amount of  
conduits!! 1,000s of  
feet of different sizes.  
Approximatley over 2  
miles of conduit  
installed when project  
is completed

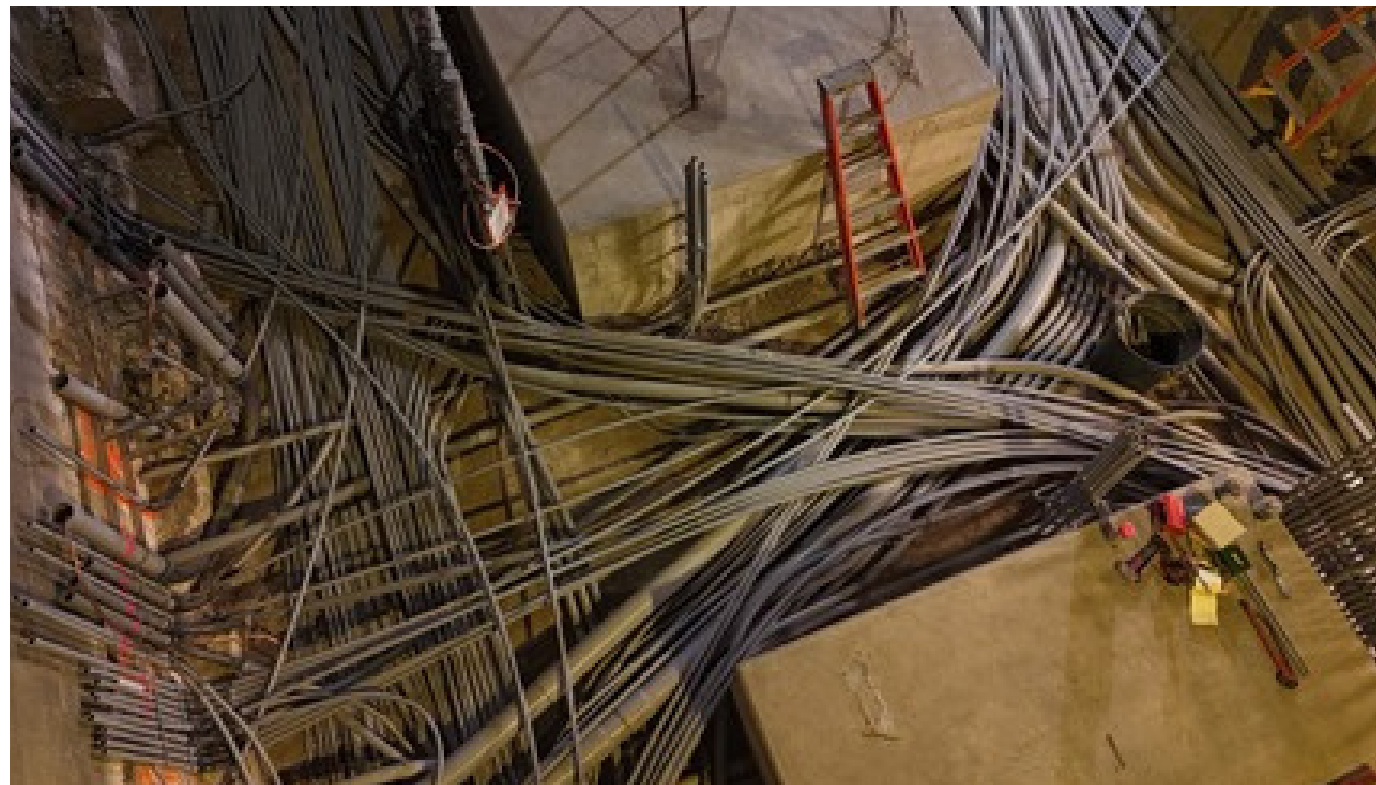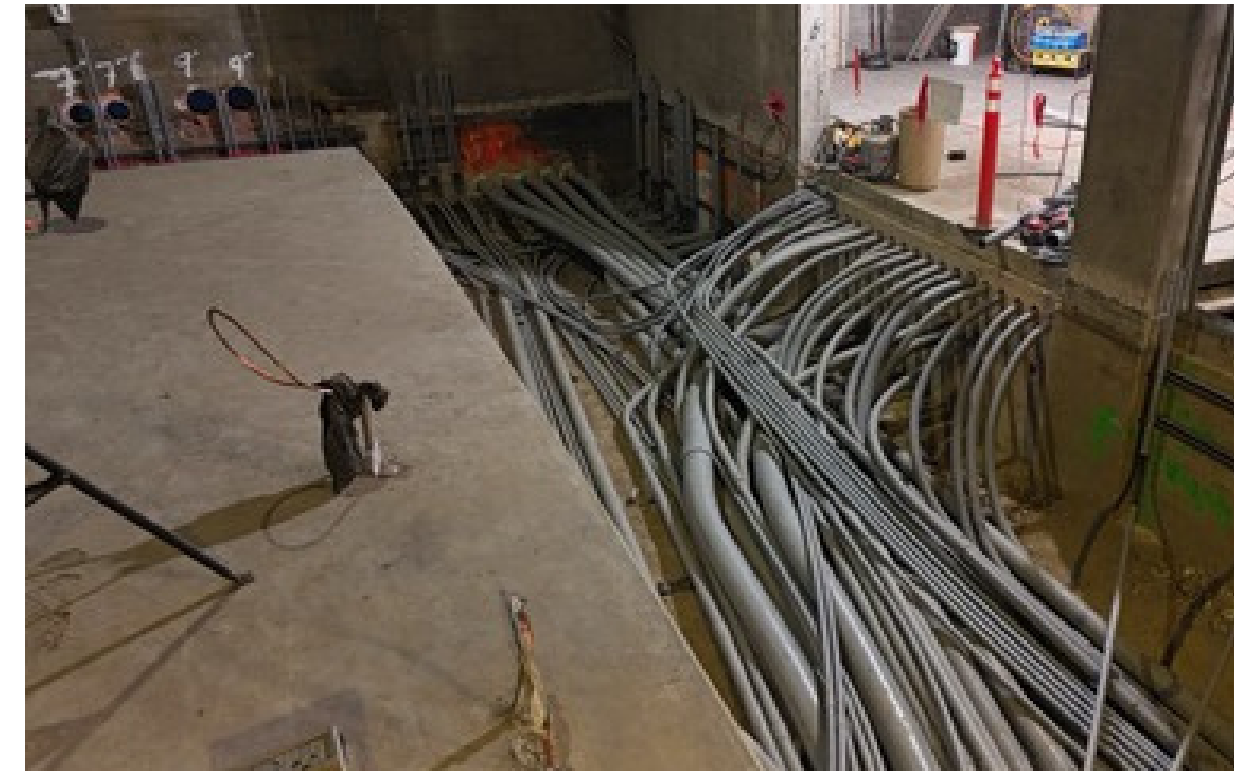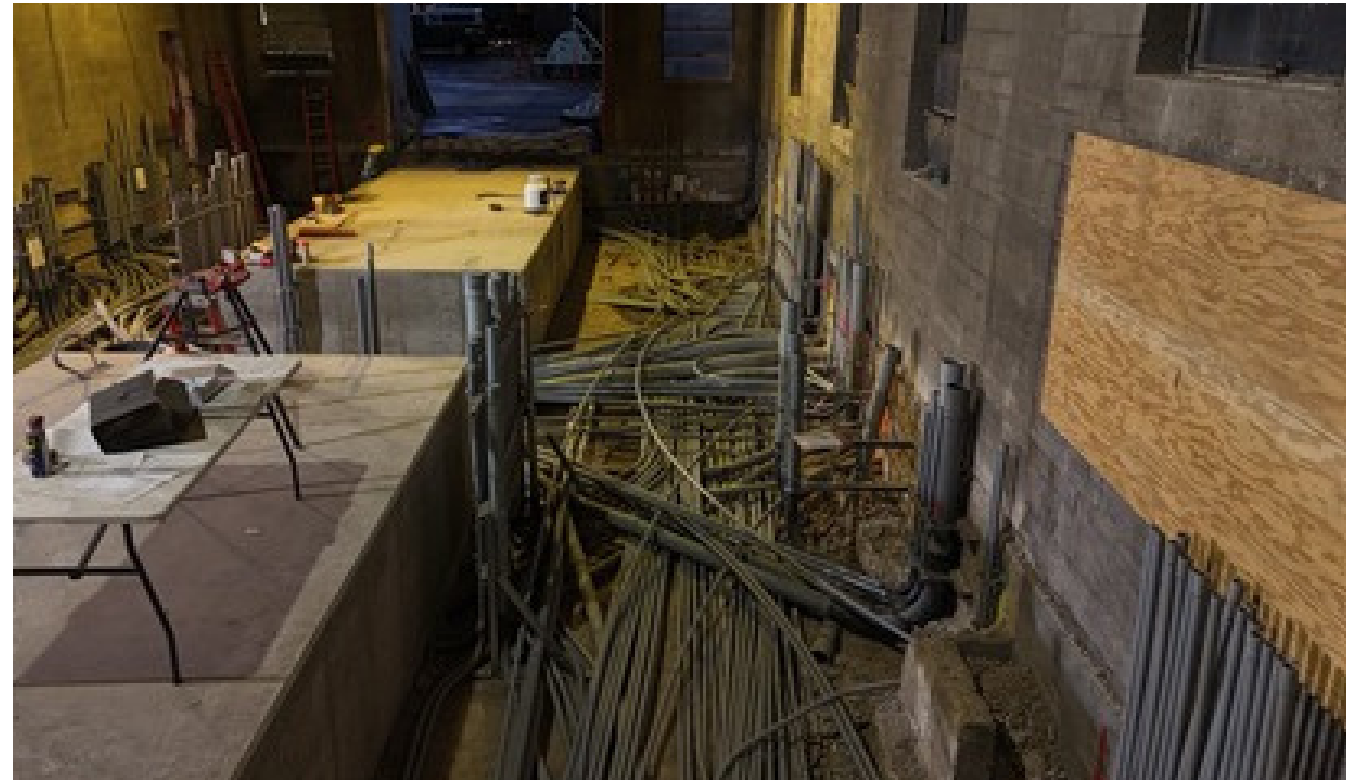





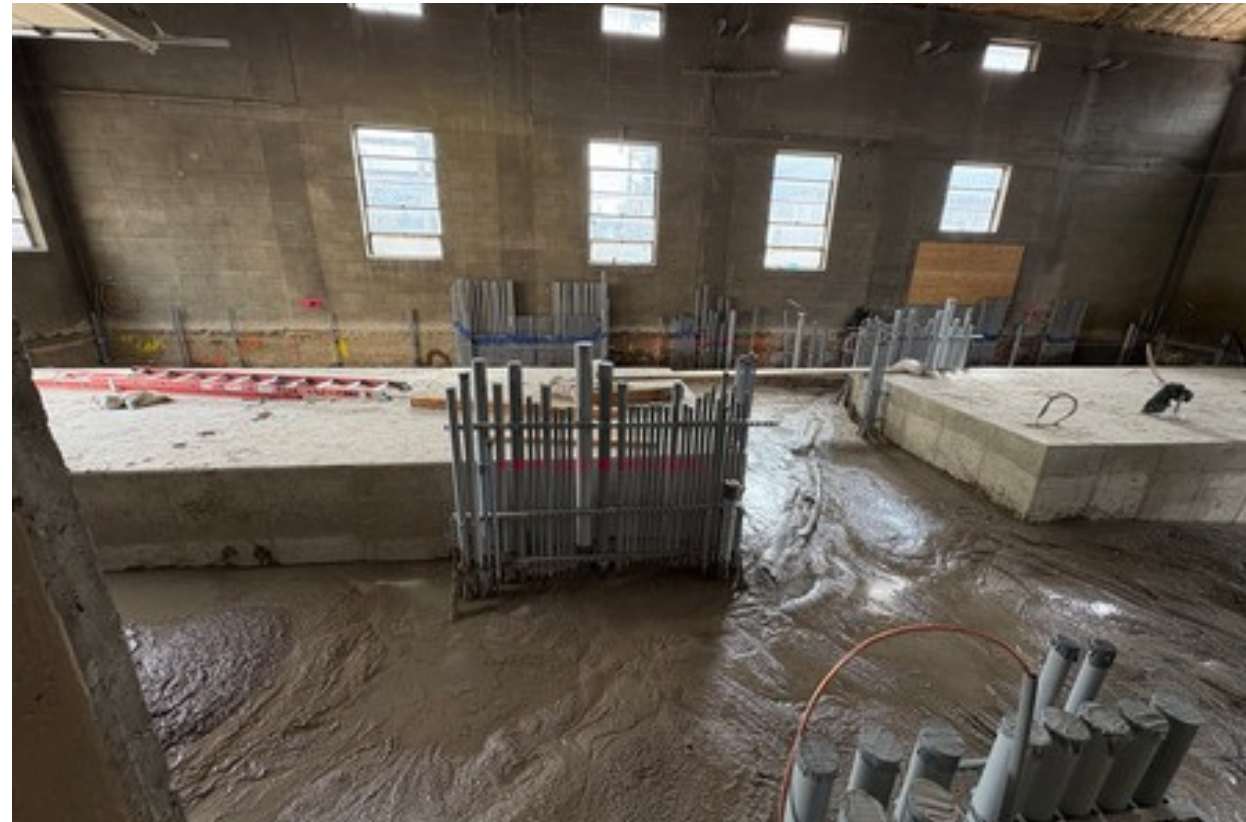

10/21/25

Road base being brought on top of  
slurry for concrete floor to be  
poured next

Slurry fill over all the conduits  
10/16/25

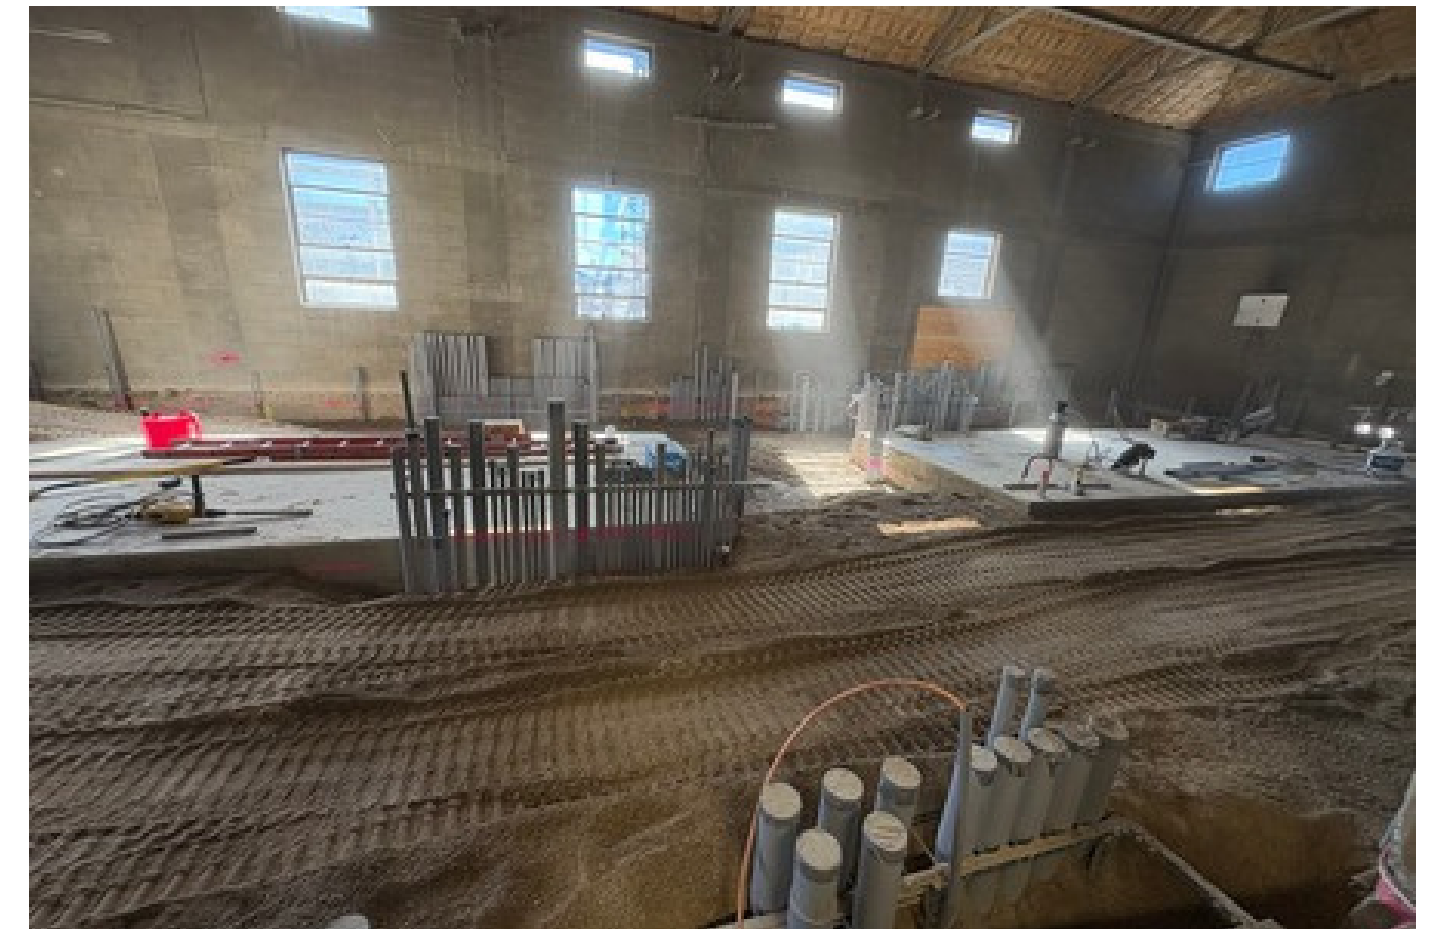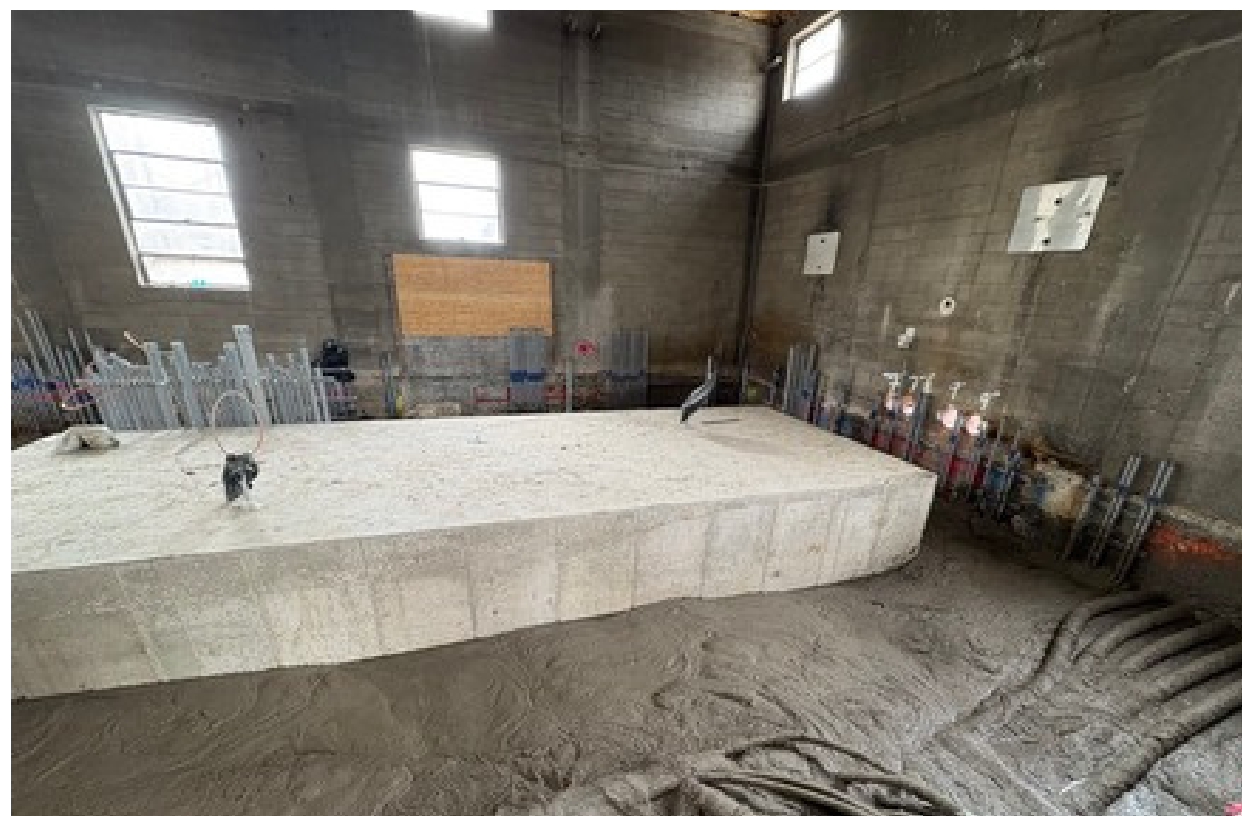






10/29/25  
10/30/25

Rebar being installed



Start of  
reroute of  
sewer line

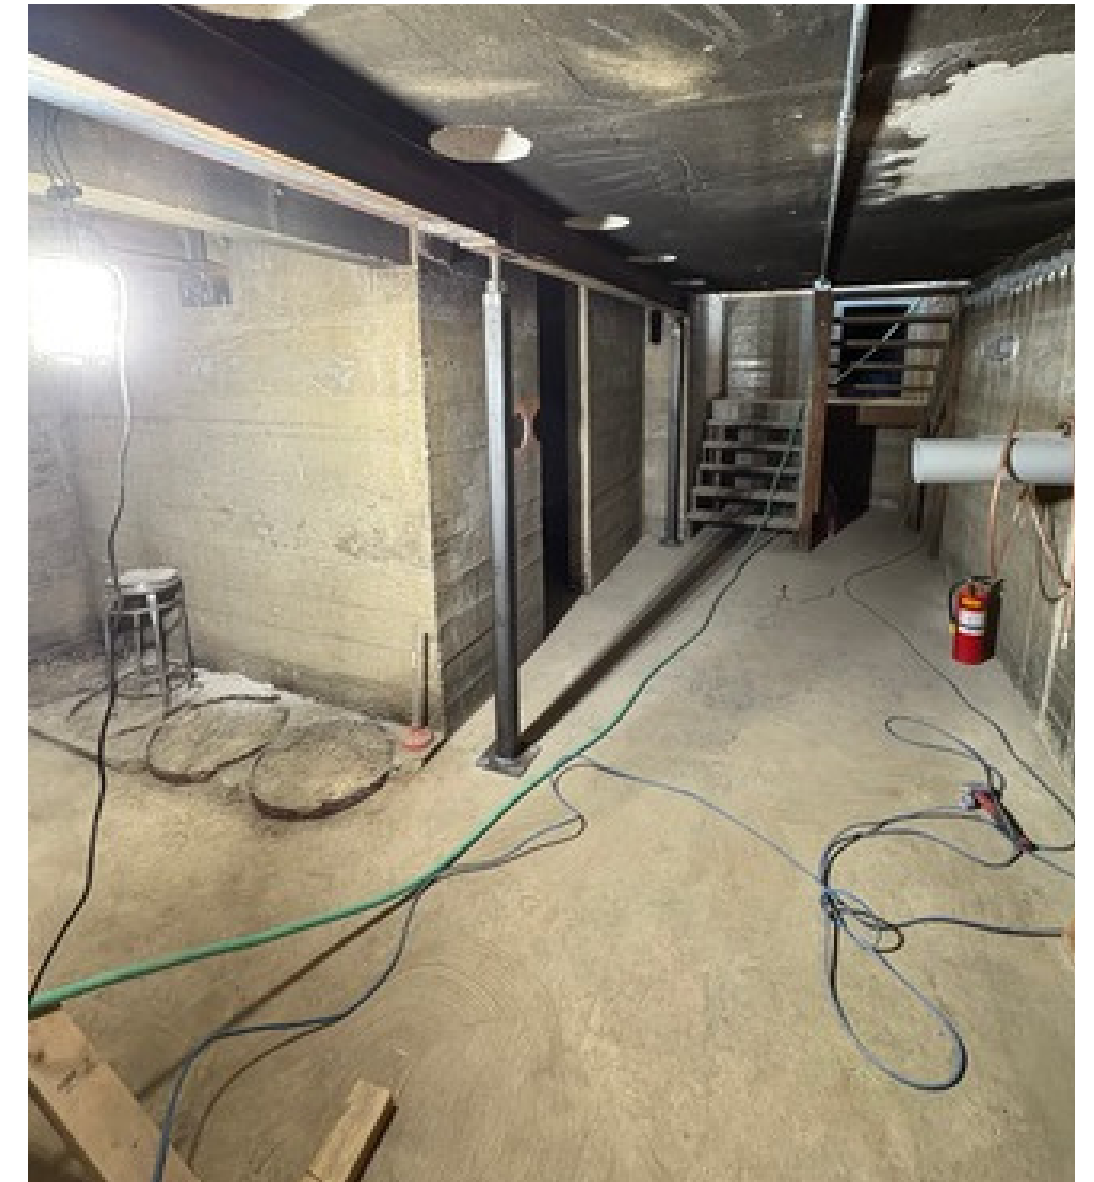

Steel Support beams  
added below  
switchgear room



Finishing up sewer line  
10/30/25



Floor being poured  
11/5/25



11/11/25  
Windows being blocked in  
with concrete.



11/24/25



Shown here window blocked in.  
1 of 8 windows



Stand installed for  
swamp cooler and  
OXY catalyst stack



**BOLD**  
**MOVES**

Generator arrived on site  
and installed in building on  
11/25/25





Exhaust  
stack and  
OXY  
catalyst  
being  
installed

11/25/25



Generator is in the building!!!!





Great  
work!





All major equipment has been delivered as of 11/26/25






Overall project to date is 65% to 70% complete  
There will still be a lot a wire to pull into the conduits.

Next steps is to get gas line connected

Main power connection into our substation

If all goes well we should be able to run power plant summer of 2026

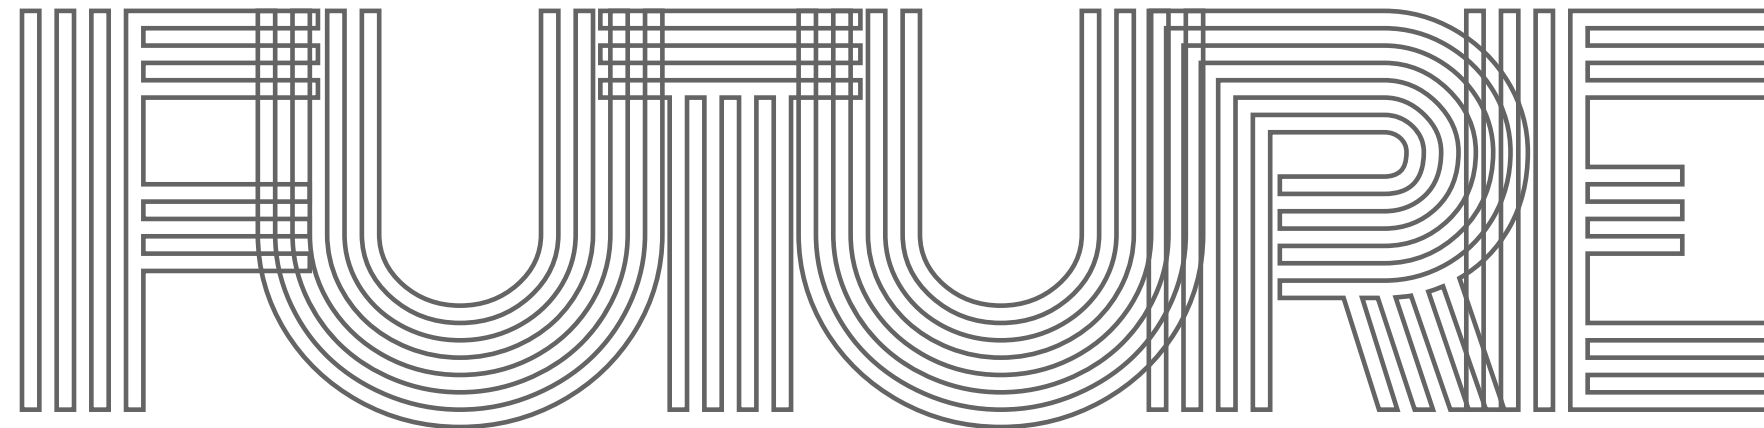

READY

Merry  
Christmas!

thank you!
