

Public Works

Flood Prep

Flood Prep

100 East Zone Protection Rebuilt berm & staged sandbags



Flood Prep


Sandbag Stations

Emma Blvd

100 East

Public Works

Rotary Park

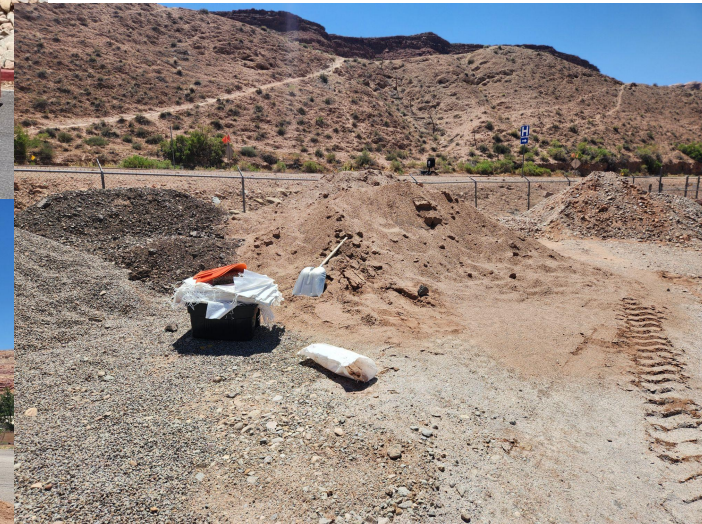

Flood Prep

Westwater Drive Detention Basin(Frog Pond)

Labor - 72

Loader - 36

5 Ton Dump - 36

Material - 40 Tons



Flood Prep

Storm Drain cleaning Utilities Assisted with 6 lines



Flood Prep

Storm Drain cleaning



Flood Prep

Sweeper

Week 1 - 72 hours

Weeks 2 & 3 - 84 hours



Flood Prep

500 West Ditch

Mowed, weedeated, trimmed & removed trees

Labor Streets & Facilities **183 hours**

Mower - **5 Hours**

Mini x - **20.5 Hours**

Backhoe - **5 Hours**

2 - 5 Ton Dump - **35 Hours**



Flood Prep

500 West Ditch

Material - 24 - 5 ton loads



Flood Prep

500 West Ditch

After



Flood Prep

500 West Ditch After



Flood Prep

500 West Ditch

Two weeks ago



Today



What's Next

500 West Ditch

Tree removal, stump grinding, remove culverts

Storm Drains

Utilities will continue to assist

Street Sweeping

Ongoing

Sandbag Stations

Ongoing

Questions?
