




Jones & DeMille  
Engineering

www.jonesanddemille.com | 800.748.5275

# MONTHLY SUMMARY

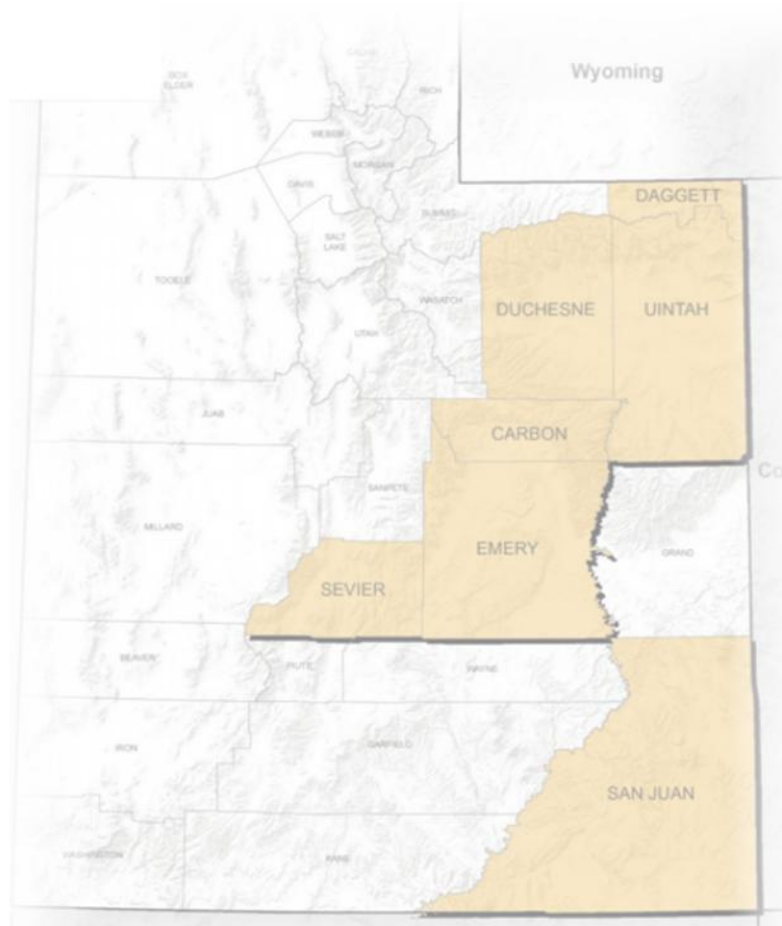

**Date:** *April 9, 2026*

**To:** *Rural Utah Infrastructure Coalition Board & Executive Director*

**From:** *Brian Barton, PE; Daniel Hawley, PE*

**Subject:** *Monthly Summary of Work for March 2026*

1535 South 100 West  
Richfield, UT 84701  
435.896.8266

50 South Main, Suite 4  
Manti, UT 84642  
435.835.4540

38 West 100 North  
Vernal, UT 84078  
435.781.1988

1675 South Highway 10  
Price, UT 84501  
435.637.8266

520 West Highway 40  
Roosevelt, UT 84066  
435.722.8267

775 West 1200 North  
Suite 200A  
Springville, UT 84663  
801.692.0219

1664 South Dixie Drive  
Building G  
St. George, UT 84770  
435.986.3622

7 South Main Street  
Suite 107/109  
Tooele, UT 84074  
435.268.8089

696 North Main Street  
PO Box 577  
Monticello, UT 84535  
435.587.9100

545 East Cheyenne Drive  
Suite C  
Evanston, WY 82930  
307.288.2005

## Active Projects

Name	Status	Directly Impacted Counties	Schedule
<b>Uinta Basin Railway (UBRY)</b>	Active Project	Uintah, Carbon, Duchesne	0-2 Years
<b>Jensen Unit Pump Station</b>	Active Project	Uintah	0-1 Years
<b>Ashley Valley Railway (AVRY)</b>	Active Project	Uintah	0-1 Years
<b>Bulk Commodity Ocean Terminal</b>	Active Project	Carbon, Emery, Sanpete, Sevier	0-1 Years

## Active Initiatives

Name	Status	Directly Impacted Counties	Schedule
<b>Utah Energy Research Lab (SRERC)</b>	Active Initiative	Carbon, Emery	1-2 Years
<b>Greendale Resort Planning</b>	Active Initiative	Daggett, Uintah	2-5 Years
<b>Navajo Mountain Regional Transportation Planning</b>	Active Initiative	San Juan	0-2 Years

## Potential Projects & Initiatives

Name	Status	Directly Impacted Counties	Schedule
<b>Natural Gas Opportunities Planning</b>	Potential Initiative	Daggett, Uintah, Duchesne, Carbon, Emery, San Juan	0-2 Years
<b>Ridge Road Industrial Park Infrastructure</b>	Potential Project	Carbon	0-2 Years
<b>Carbon Fiber Opportunities Planning</b>	Potential Initiative	Carbon, Emery, Sevier	0-3 Years
<b>Air Quality Solutions Study</b>	Potential Initiative	Daggett, Uintah, Duchesne, Carbon, Emery, Sevier, San Juan	1-2 Years
<b>Rural Utah Energy Ecosystem (RUEE)</b>	Potential Initiative by others	Carbon, Emery, Daggett, Uintah, Duchesne, Sevier, San Juan	0-2 Years
<b>Leland Bench Utilities (water, gas, power)</b>	Potential Project	Uintah, Duchesne	2-5 Years
<b>Southeast Utah Rail Line Study</b>	Potential Project	San Juan, Grand	2-5 Years
<b>Lake Powell Bridge Crossing</b>	Potential Project	San Juan	5+ Years
<b>Regional Natural Gas Transmission Pipeline Improvements</b>	Potential Project	Emery, Carbon, Duchesne, Uintah	0-2 Years
<b>Rural Freight Transportation Study (Phase 2)</b>	Potential Project	Sevier, Daggett, Uintah, Duchesne, Carbon, Emery, San Juan	1-2 Years
<b>Power Generation Facility Planning</b>	Potential Initiative	Sevier, Daggett, Uintah, Duchesne, Carbon, Emery, San Juan	1-2 Years
<b>Eastern Utah Regional Connection Planning</b>	Potential Project	Uintah, San Juan, Daggett, Duchesne	2-5 Years
<b>Regional Recreation Planning</b>	Potential Project	Daggett, Uintah, Duchesne, Carbon, Emery, Sevier, San Juan	2-5 Years
<b>Salt Valley Road to Arches</b>	Potential Project	San Juan, Emery, Grand, Wayne, Carbon	0-2 Years
<b>Uinta Basin Economic Impact Study</b>	Potential Initiative	Daggett, Duchesne, Uintah	0-2 Years

<b>Zero-CO2 Emissions Industrial Hub</b>	Potential Initiative	Duchesne, Uintah	1-2 Years
--	----------------------	------------------	-----------

### Completed Projects

<b>Name</b>	<b>Status</b>	<b>Directly Impacted Counties</b>	<b>Year</b>
<b>Swinging Bridge</b>	Complete	Daggett	2015
<b>Fiber in Daggett County</b>	Complete	Daggett	2016
<b>San Juan County Fiber</b>	Complete	San Juan	2018
<b>Rural Freight Transportation Study (Phase 1)</b>	Complete	Sevier	2021
<b>Seep Ridge Road Surface Seal</b>	Complete	Uintah, Daggett, Duchesne	2023
<b>San Rafael Energy Research Center</b>	Complete	Emery, Carbon	2023
<b>Utah Navajo Water Settlement Planning</b>	Complete	San Juan	2025

***We appreciate the opportunity to work closely with the Coalition on so many critical projects in the region. The following is the summary of our work completed during the past month.***

## Rural Utah Infrastructure Coalition – Uinta Basin Railway (UBRY)



### **1. Phase – 12 – Phase 2 Owner’s Representative Services / GRAMA Requests**

- Legal coordination
- BUILD grant coordination
- Ute Tribe coordination
- SITLA coordination
  
- GIS data coordination
- Ongoing team meetings
- Executive Director support
- Budget tracking and management

### **2. Phase – 13 – Strategic Communications**

- General media relations
- Report inquiries
- Local contractor coordination
- Social analytics analysis and responses
- Stakeholder meeting and coordination

### **3. Phase – 40 – BIA Draft Record of Decision Prep**

- BIA staff coordination
- Section 7 coordination
- Cactus survey coordination
- Ridge cross survey coordination
- Tribe packet Prep
- POD preparation

## Rural Utah Infrastructure Coalition – Program Management & Engineering Services

### **1. Phase – 30 – General Services**

- Board meeting preparation, coordination, and execution
- General budget coordination
- Work on updated Coalition boundary legal description
- Project tools review
- Team coordination

### **2. Phase – 35 – Strategic Communications**

- Board meeting preparation and website updates
- Branding review

# Rural Utah Infrastructure Coalition – 2025 Jensen Unit Pump Station Planning

## **3. Phase – 30 – Concept Planning**

- Project planning

## Rural Utah Infrastructure Coalition – Ocean Terminal Planning

### **4. Phase – 30 – Planning & Studies**

- Longview site visit

## Rural Utah Infrastructure Coalition – Greendale Resort Planning

### **5. Phase – 30 – Planning & Studies**

- Review water requirements
- Coordination with MLEA
