

**DOCUMENT 00 94 10
CHANGE ORDER****Change Order No. 6**

Date of Issuance: 31 July 2026

Owner: PCC Land

Owner's Contract No.:

Contractor: BHI, Inc

Contractor's Project No: 26352-2500

Engineer: Horrocks

Engineer's Project No.: 2024-0063

Project: Promontory Lift Station

The Contract is modified as follows upon execution of this Change Order:

Description: Proposed generator required additional ventilation to run in the enclosed space.
Increased cost to install vents along wall and reinforce lintels.

Attachments: Promontory Lift Station – Change Proposal #013

CHANGE IN CONTRACT PRICE	CHANGE IN CONTRACT TIMES
Original Contract Price: \$ 12,545,244.59	Original Contract Times, dates: Substantial Completion: 01 October 2026 Ready for Final Payment: 29 October 2026
Increase from previously approved Change Orders No. 1 to No. 5 \$ 381,007.04	Increase from previously approved Change Orders No. 1 to No. 5, days: Substantial Completion: 74 Ready for Final Payment: 74
Contract Price prior to this Change Order: \$ 12,926,251.63	Contract Times prior to this Change Order, dates Substantial Completion: 14 December 2026 Ready for Final Payment: 11 January 2027
Increase of this Change Order: \$ 11,095.00	Increase of this Change Order, days: Substantial Completion: Ready for Final Payment:
Contract Price incorporating this Change Order: \$ 12,937,346.63	Contract Times with all approved Change Orders: Substantial Completion: 14 December 2026 Ready for Final Payment: 11 January 2027

RECOMMENDED:

By:



Engineer

ACCEPTED:

By:


Trent Fryhling
Contractor (Authorized
Signature)AUTHORIZED: DocuSigned by:

By:


Daniel Stephens
Owner's Authorized Signature)

Title: Project Manager

Title: Project Manager

Title: Manager

Date: 31 July 2026

Date: 8/06/2026

Date: 8/17/2026

Approved by Funding Agency (if applicable)



By: _____ Title: _____ Date: _____

END OF DOCUMENT

EJCDC® C-941, Change Order.

Copyright © 2018 National Society of Professional Engineers, American Council of Engineering Companies,
and American Society of Civil Engineers. All rights reserved.



**BUILDING RELATIONSHIPS
ONE PROJECT AT A TIME**

CONSTRUCTION MANAGEMENT > FACILITIES & PIPELINE > CIVIL & EXCAVATION > INSTRUMENTATION & ELECTRICAL > WIRELESS & COMMUNICATIONS

To: PCC Land, LLC Address: 221 25th Street Suite 213 Ogden, UT 84401	Contact: Phone: Email:				
Project Name: 26352-2500 UT_PCCLand LLC_PLS Add. Louvers And Reinforc. PCO-013 Project Location:	Bid Number: 95025-07-04 Bid Date: 6/18/2026				
Item #	Item Description	Estimated Quantity	Unit	Unit Price	Total Price
01	Additional Louvers And Reinforcement	1.00	LS	\$11,095.00	\$11,095.00
Total Bid Price:					\$11,095.00

Payment Terms:

Payment due within 30 days of date of invoice, regardless of when payment is made by Owner.

 7/8/26

ACCEPTED: The above prices, specifications and conditions are satisfactory and hereby accepted. Buyer: _____ Signature: _____ Date of Acceptance: _____	CONFIRMED: BHI Authorized Signature: _____ Estimator: Trent Fryhling 435-790-5788 tfryhling@bhico.com
---	---

INDUSTRY EXCELLENCE
POWERED BY VALUES®



BUILDING RELATIONSHIPS ONE PROJECT AT A TIME

Project Name:

Promontory Lift Station

BHI Project Number:

26352-6500

Owner Name:

Promontory Commerce Center PID No.1

COR Description:

Louver Add

COR#

02

Scope of Work

Added Louvers in the CMU for the generator room

Subcontracted Work

Description of Work	Subcontractor Name	Bid Price
(4) Added Louvers in the Generator Room	KHI	\$ 8,384.00
Shoring/Lintels for Louver work	Rocky Mountain Masonry	\$ 1,200.00
	Subtotal	\$ 9,584.00

Mark up and Profit per subcontract terms 10% \$ 958.40

Total Price of Extra \$ 10,542.40
Additional Calendar Days 0

Cody Gillette


BHI

06/17/2026

Date

DIV 25. Trent Fryling

Date



KHI Mechanical Services

2630 South 3270 West, Suite B
West Valley City, UT 84119

Phone: (801) 972-2680
Fax: (801) 972-2685

Mr. Cody Gillett
BHI Construction
1175 E 2000 S
Vernal, UT 84078
email: cgillett@bhico.com

May 18, 2026

RE: Lift Station - Generator Room Added Louvers

KHI Project # C1888

Dear Cody Gillett

KHI CO # 2

We are pleased to provide you with the following proposal to supply equipment, material, and labor required to perform the following work:

Tax Rate: **1.0835** (Utah)

Item #	Description	Equip no tax	Material no tax	Field Rate	Field Manhour	Field Cost	Subcon	Other	Total w/ tax
1	Deduct Underground Piping & Install		\$ (300)	\$ 90	-5.50	\$ (495)			\$ (820.05)
2	Deduct Sump Pump	\$ (297)		\$ 90		\$ -			\$ (322.12)
3	(4) Added Louvers In Generator Room	\$ 4,810	\$ 600	\$ 90	20.00	\$ 1,800			\$ 7,661.74
				\$ 90		\$ -			\$ -
				\$ 90		\$ -			\$ -
				\$ 90		\$ -			\$ -
				\$ 90		\$ -			\$ -
				\$ 90		\$ -			\$ -
				\$ 90		\$ -			\$ -
				\$ 90		\$ -			\$ -
	Permits								\$ -
	Set Up and Clean Up			\$ 90	2.00	\$ 180			\$ 180.00
	Material Handling & Delivery			\$ 90	2.00	\$ 180			\$ 180.00
	Supervision			\$ 95	3.00	\$ 285			\$ 285.00
	Engineering			\$ 105		\$ -			\$ -
	Project Management			\$ 105	3.00	\$ 315			\$ 315.00
	Storage					\$ -			\$ -
	Subsistence					\$ -			\$ -
	Rental			\$ 95	1.00	\$ 95			\$ 95.00
	Check/Test/ Start up			\$ 95		\$ -			\$ -
	Payment & Performance Bond					\$ -			\$ -
	Warranty			\$ 95	0.50	\$ 48			\$ 47.50
	Other					\$ -			\$ -
Sub Total		\$4,513	\$ 300		26.00	\$ 2,408	\$ -	\$ -	\$ 7,622
Tax		\$ 377	\$ 25						
Totals w/ Tax and Overhead		\$ 4,890	\$ 325			\$ 2,408	\$ -	\$ -	
Cost w/ Tax & Overhead		\$ 7,622							
MU (by %)		10%							
TOTAL		\$ 8,384							

If you have any questions or require additional information, please give me a call.

Sincerely,
KHI Mechanical,

Colin Price
Project Manager

Rocky Mountain Masonry Inc.
 3389 South 1575 West. Ogden, UT
 84401
 www.rockymountainmasonryinc.com
 Office: 801-622-2630
 Dan@rmmbrick.com Cell
 801-725-7330
 Colton@rmmbrick.com Cell
 801-710-7170



Number PromontoryLSTS

Date 6/17/2026

Bid To

Cody Gillett

cgillett@bhico.com

Project

Promontory Lift Station

PR- Provide Temporary shoring for Openings and Mechanical Louvers

Proposal based on plans and directive and addendum# valid for 90 days

Description

Proposal Includes: Labor, Equipment, Safety and Supervision To Furnish and install
 Temporary shoring for (4) 6'x2' mechanical louvers.

\$1,200.00


Excludes- insulation, angle irons, hollow metal door frames, temporary shoring. Items
 installed but not supplied; rebar, loose placed angle irons and miscellaneous steel
 embedded items. Our proposal does not include any overtime work/after hours work

\$1,200.00

Signature:

Date:

UTB3-NF | 08:11 AM TUESDAY 21 APRIL 2026 | C:\BLACKPINE\TEMP\SHEETS\14 A102.DWG

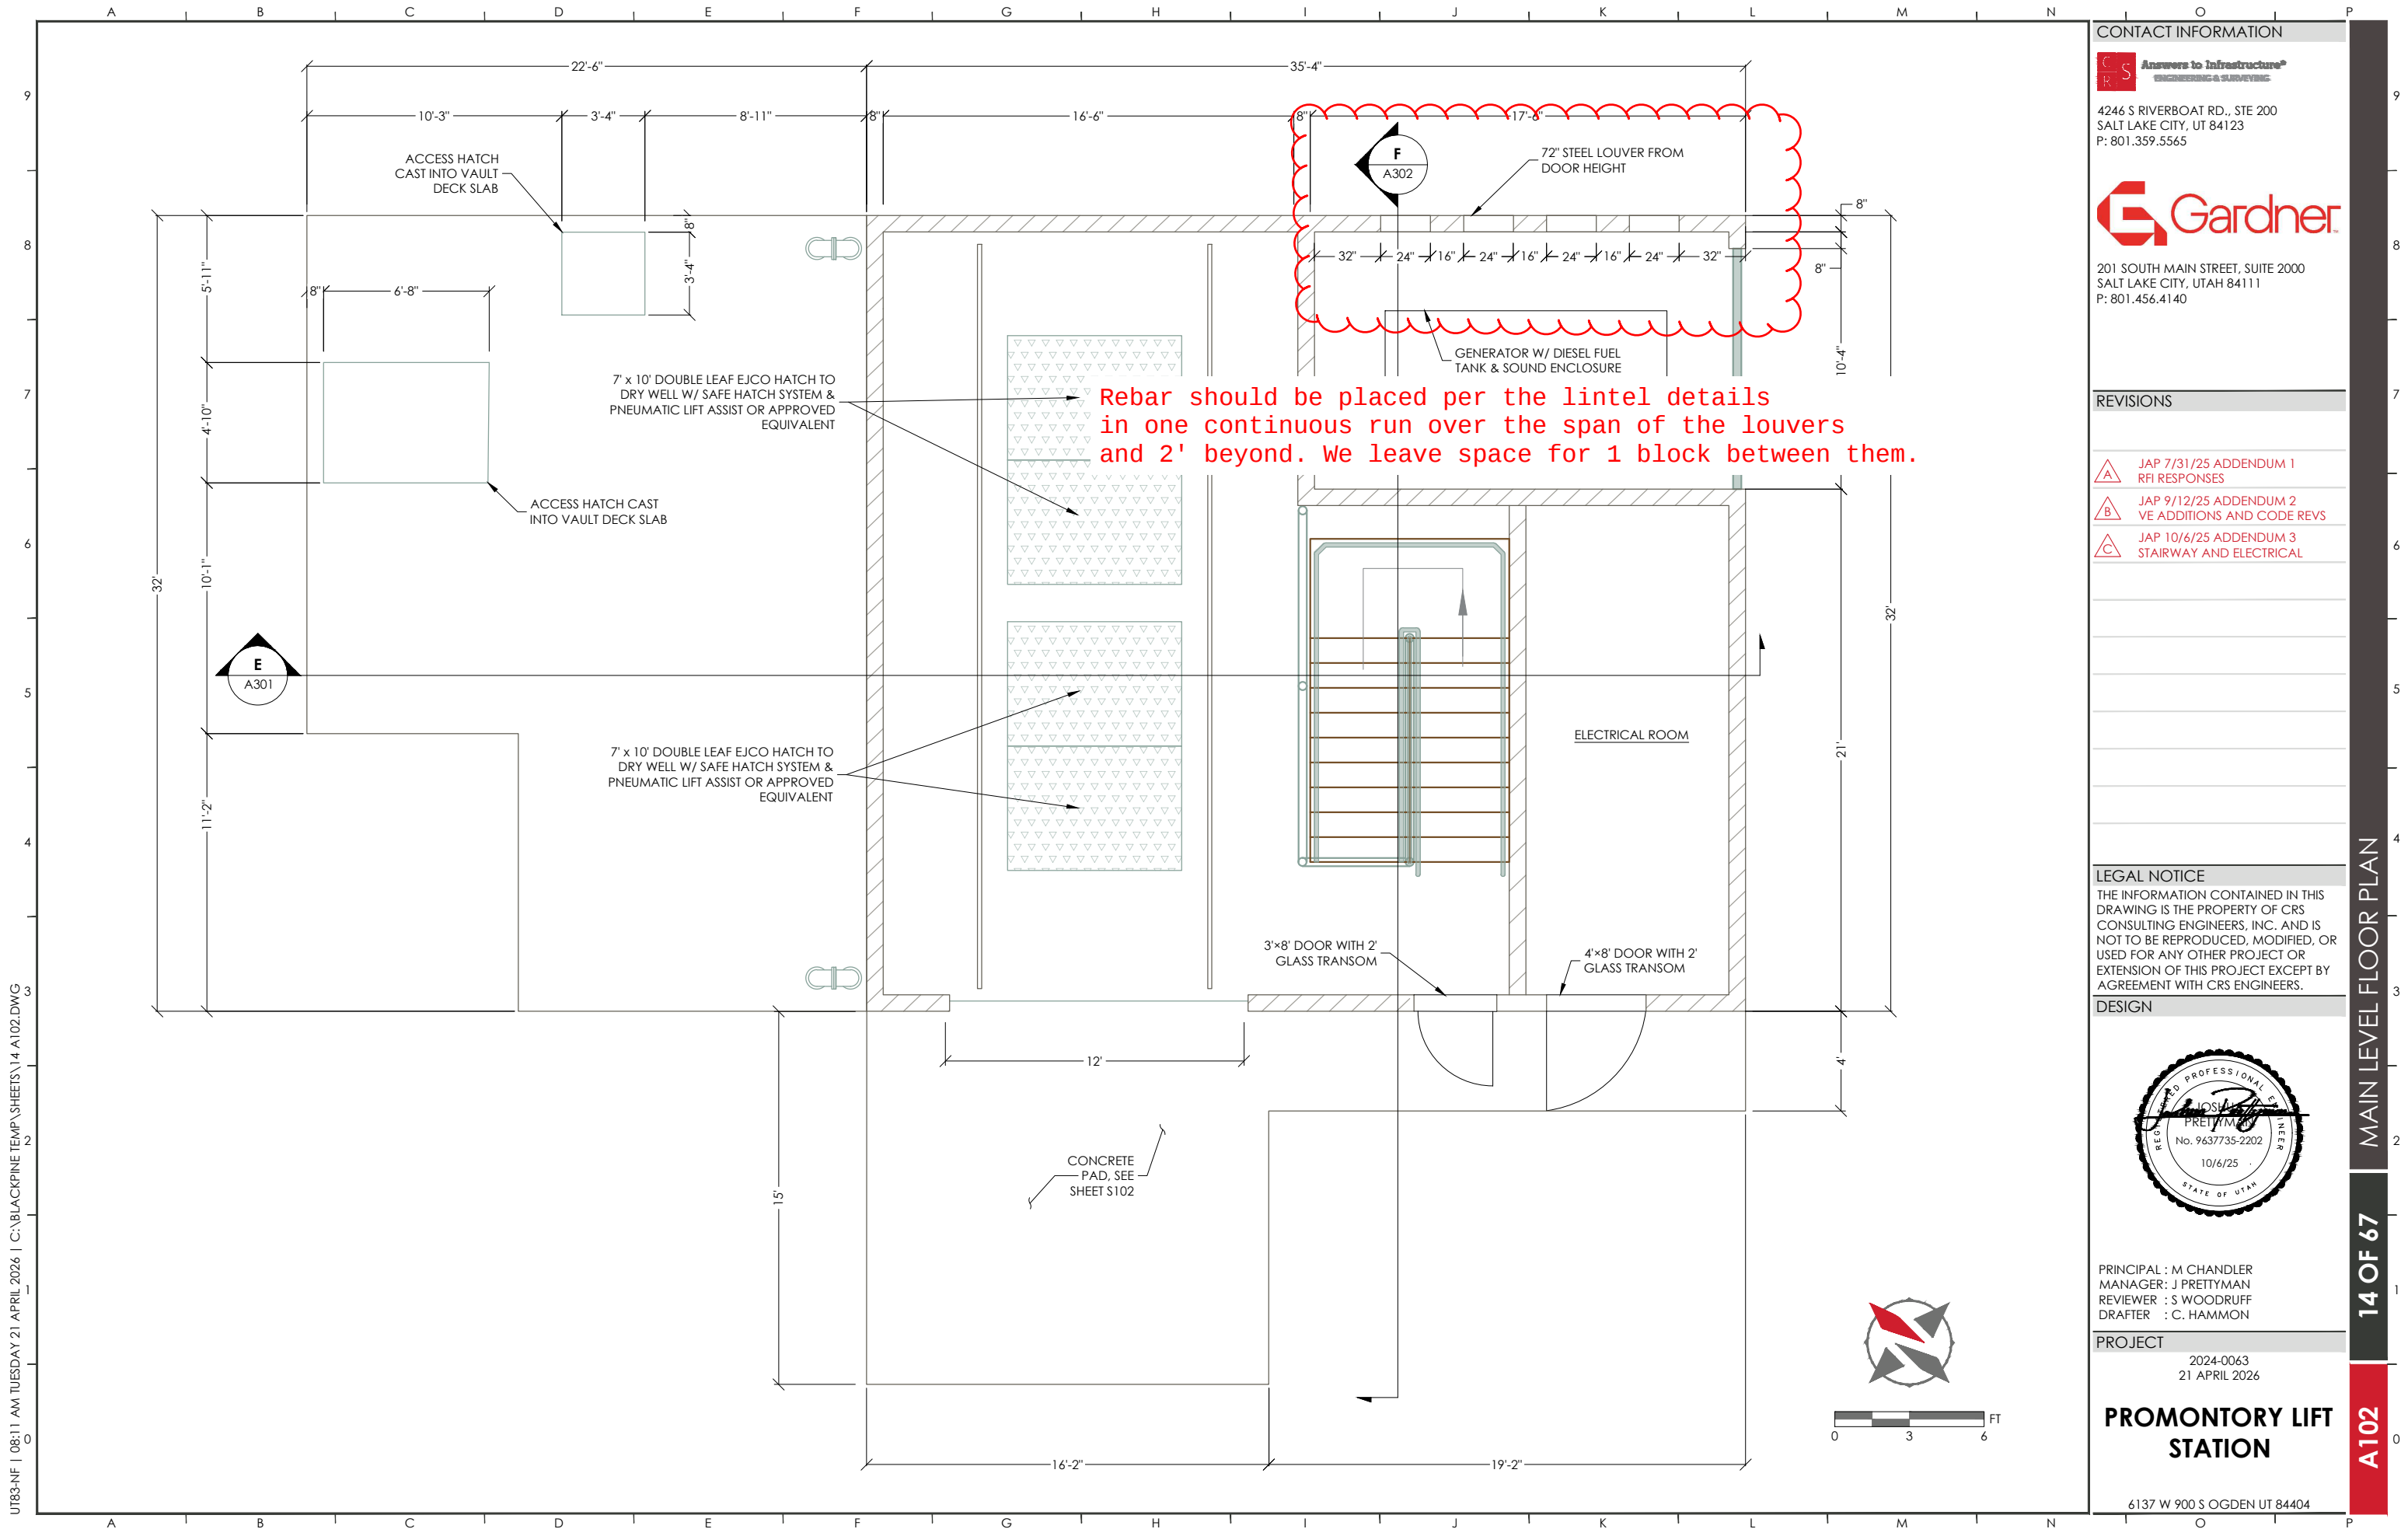

CONTACT INFORMATION

CRS Answers to Infrastructure®
ENGINEERING & SURVEYING
4246 S RIVERBOAT RD., STE 200
SALT LAKE CITY, UT 84123
P: 801.359.5565



201 SOUTH MAIN STREET, SUITE 2000
SALT LAKE CITY, UTAH 84111
P: 801.456.4140


REVISIONS

- A** JAP 7/31/25 ADDENDUM 1
RFI RESPONSES
- B** JAP 9/12/25 ADDENDUM 2
VE ADDITIONS AND CODE REVS
- C** JAP 10/6/25 ADDENDUM 3
STAIRWAY AND ELECTRICAL

LEGAL NOTICE

THE INFORMATION CONTAINED IN THIS
DRAWING IS THE PROPERTY OF CRS
CONSULTING ENGINEERS, INC. AND IS
NOT TO BE REPRODUCED, MODIFIED, OR
USED FOR ANY OTHER PROJECT OR
EXTENSION OF THIS PROJECT EXCEPT BY
AGREEMENT WITH CRS ENGINEERS.

DESIGN



PRINCIPAL : M CHANDLER
MANAGER: J PRETTYMAN
REVIEWER : S WOODRUFF
DRAFTER : C. HAMMON

PROJECT

2024-0063
21 APRIL 2026

**PROMONTORY LIFT
STATION**

6137 W 900 S OGDEN UT 84404
